

Work Order ID 50980

July 28, 2009 1:55:32 PM



Page 1

Item ID: D212-664-101

Accept



Setup Start



Revision ID: C

Stop



Item Name: Crosstube Fwd

Start Date: 7/30/09 Start Qty: 1.00



Cust Item ID:

Required Date: 8/14/09 Req'd Qty: 1.00

Customer:

Reference:

Approvals:

Process Plan:

Date:

Tooling:

Date:

Run Start



QC:

Date:

SPC (Y/N):

Date:

Stop



Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Draw
Number

Draw
Rev.

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

Draw Nbr

Revision Nbr

D212-664-141

Rev C

100

0.00



DC

Document Control

DOCUMENT CONTROL

Memo

Photocopy bluefile and create labels as per PPP D212-664-101 CHG003

HJ for BG 08/02/01

S 08/02/01

110

Pick Kit

0.00



Packaging

Packaging

Memo

0.00

Packaging

PC9/8/31 C

120

0.00



CNC Bend 2

BENDING MACHINE - CROSSTUBES

Memo

0.00

CNC Alpha 160 Bender

Bend tube as per Dwg D212-664-141 using CNC bender program 212-fw and Folio FT015

9-8-14

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 50980

July 28, 2009 1:55:32 PM

Page 2

Item ID: D212-664-101

Accept

Setup Start

Revision ID: C

Stop

Item Name: Crosstube Fwd

Start Date: 7/30/09 Start Qty: 1.00

Cust Item ID:

Required Date: 8/14/09 Req'd Qty: 1.00

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run HoursDraw
NumberDraw
Rev.Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

130

QC15- Crosstube Dimensional Check

0.00

QC

Memo

0.00

Quality Control

140

Crosstubes

0.00

Crosstubes

Memo

0.00

Crosstubes

1-Drill pilot holes in tube as per Dwg D212-664-141 using drill Jig DT8548 & DT8549

2-Ream hole to finish size in tube as per Dwg D212-664-141 using drill Jig DT8548 & DT8549. Check dimensions between holes, both sides on both cuffs, to ensure alignment with saddle holes.

3-Scribe part # and batch # using vibrating stylus as per Dwg D212-664-141

4-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D212-664-141

-ANM 9-5-14

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 50980

July 28, 2009 1:55:32 PM

Page 3

Item ID: D212-664-101

Accept

Setup Start

Revision ID: C

Stop

Item Name: Crosstube Fwd

Start Date: 7/30/09 Start Qty: 1.00

Cust Item ID:

Required Date: 8/14/09 Req'd Qty: 1.00

Customer:

Reference:

Run Start

Approvals: Process Plan: Date: Tooling: Date:

Stop

QC: Date: SPC (Y/N): Date:

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	----------------	--------------	--------------	---------------	---------------	------------------	----------------

150

Crosstubes Chemical Conversion

0.00



HandFXtube

Memo

0.00

Hand Finishing Crosstubes

Chemical Conversion Coat within 24 hours of bending and drilling

1 9 - Aug 8-9-17

160

QC5- Inspect part completeness to step on W/O

0.00



QC

Memo

0.00

Quality Control

=> 8/9/06/17

④ f

170

Outsource process - NDT per QSI038 4.1

0.00



Outsource2

Memo

0.00

Outsource process - NDT

Liquid Penetrant Inspection as per QSI 038

Issue P/O: 10220

LPI as per ASTM 1417 Level 2

Attach copy of NDT results to work order

CZ 09/08/19 ①

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 50980

July 28, 2009 1:55:32 PM



Page 4

Item ID: D212-664-101

Accept



Setup Start



Revision ID: C

Stop



Item Name: Crosstube Fwd

Start Date: 7/30/09 Start Qty: 1.00



Cust Item ID:

Required Date: 8/14/09 Req'd Qty: 1.00



Customer:

Reference:

Run Start



Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Stop



QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Draw
Number

Draw
Rev.

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

180



Packaging

Packaging

Receive & Inspect for Damage & Mat'l Certs
Packaging

0.00

Memo

0.00

Ensure copy of NDT results attached to work order.

LC 9/8/08 (1)

190



QC

Quality Control

QC5- Inspect part completeness to step on W/O

0.00

Memo

0.00

Inspect for damage & ensure results are as per Dwg D212-664-141

MA 08 19 (1)

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 50980

July 28, 2009 1:55:32 PM



Page 5

Item ID: D212-664-101

Accept



Setup Start



Revision ID: C

Stop



Item Name: Crosstube Fwd

Start Date: 7/30/09 Start Qty: 1.00



Cust Item ID:

Required Date: 8/14/09 Req'd Qty: 1.00



Customer:

Reference:

Run Start



Approvals: Process Plan: Date: Tooling: Date:

Stop



QC: Date: SPC (Y/N): Date:

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Draw
Number

Draw
Rev.

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

200

Spray Painting per QSI005 4.2

0.00



SprayPaint

SprayPaint

Memo

0.00

Spray Painting

1-Prime inside and outside crosstube as per QSI 005 4.2
2-Paint outside crosstube with White Imron as per QSI 005 4.2

IT 09-08-20

PRIME:

Start Time: 7:00
Finish Time: 9:00

PAINT:

Start Time: 3:00
Finish Time: 4:15

210

QC14- Inspect Spray Paint

0.00



QC

Memo

0.00

Quality Control

Then, Wrap in plastic bag to protect from scratches

ml 09 08 21 ①

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 50980

July 28, 2009 1:55:32 PM



Page 6

Item ID: D212-664-101

Accept



Setup Start



Revision ID: C

Stop



Item Name: Crosstube Fwd

Start Date: 7/30/09 Start Qty: 1.00



Cust Item ID:

Required Date: 8/14/09 Req'd Qty: 1.00



Customer:

Reference:

Run Start



Approvals: Process Plan: Date: Tooling: Date:

Stop



QC: Date: SPC (Y/N): Date:

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Draw
Number

Draw
Rev.

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

220



Crosstubes

Crosstubes

0.00

Memo

0.00

1- Lightly scuff the bonded area using a 320 grit sand paper and clean the area with 41058 wash 'n' wipe
2-Install supports with magnobond as per QSI 015 Adhere for 12 Hrs
A/R 6398 Magnobond Batch: 11/24/9 exp: 02/2010

MA 09 08 27 ①

Torque: 09 08 28 ① MA

230



QC

Quality Control

QC5- Inspect part completeness to step on W/O

0.00

Memo

0.00

=) 509/09/31

④ \$

240



Packaging

Packaging

Pick Kit

0.00

Memo

0.00

129/09/31 ①

B50980

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 50980

July 28, 2009 1:55:32 PM

Page 7

Item ID: D212-664-101

Accept

Setup Start

Revision ID: C

Stop

Item Name: Crosstube Fwd

Start Date: 7/30/09 Start Qty: 1.00

Cust Item ID:

Required Date: 8/14/09 Req'd Qty: 1.00

Customer:

Reference:

Approvals: Process Plan: Date: Tooling: Date:

Run Start

QC: Date: SPC (Y/N): Date:

Stop

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Draw
Number

Draw
Rev.

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

250

QC4- 100% Inspect kits for completeness

0.00

QC

Memo

0.00

Quality Control

260

Packaging

0.00

Packaging

Memo

0.00

Packaging

Identify and pack for shipping as per PPP D212-664-101

270

QC21- Final Inspection - Work Order Release

0.00

QC

Memo

0.00

Quality Control

② p

9/9/3 ⑩ 98

09/09/03 HJ

09-9-02

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

July 28, 2009 1:55:31 PM

Page 1

Work Order ID: 50980



Parent Item: D212-664-101RevC



Parent Item Name: Crosstube Fwd

Start Date: 7/30/09

Required Date: 8/14/09

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	--------------------------	---------------	----------------	--------

D212-664-
101TRNRevC

Manufactured No

110

Each

2.0000

1.0000



Crosstube Turning Detail



B-50992

MA 09-08-14

Warehouse

Loc Qty

Loc Code

Location

Main Warehouse

FG

2

50568

1

50569

1

D3595-063-450RevA

Manufactured No

220

Each

47.8000

4.2105



RUBBER CUSHION



Warehouse

Loc Qty

Loc Code

Location

Main Warehouse

ST

47.8

38959

2

43210

4.8

46465

41

MA 09 08 27

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

July 28, 2009 1:55:31 PM

Work Order ID: 50980

Parent Item: D212-664-101RevC

Parent Item Name: Crosstube Fwd


Comments:

Start Date: 7/30/09

Required Date: 8/14/09

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
MS21920-25		Purchased	No			220	Each	156.0000	4.0000			
<div>  </div>												
Clamp(per MIL-DTL-8783C)												

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST	156
107456	2
108111	3
108975	17
109181	48
109644	10
111282	50
111429	25
111883	1

ml 09 08 27

~~ml 09 08 27~~

D2893-1RevB

Manufactured No



2.75 Support

220 Each 72.0000 2.0000



Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST	72
25657	6
43479	10
46488	18
47109	18
47637	20

ST 09-08-26

42 ml 09 08 27

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

July 28, 2009 1:55:31 PM

Work Order ID: 50980



Parent Item: D212-664-101RevC



Parent Item Name: Crosstube Fwd

Start Date: 7/30/09

Required Date: 8/14/09

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D3428-1RevA 		Manufactured	No			250	Each	56.0000	1.0000			
Placard												

9/14/31

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST 16

47310 6

48359 10

Main Warehouse

ST096 40

50790 40

53990

AN6-35A

Purchased

No



BOLT

250 Each

34.0000 4.0000



9/14/31 (1)

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST 34

111605 34

11/23/14

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

July 28, 2009 1:55:31 PM

Page 4

Work Order ID: 50980

Parent Item: D212-664-101RevC

Parent Item Name: Crosstube Fwd



Comments:

Start Date: 7/30/09

Required Date: 8/14/09

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
AN6-36A		Purchased	No			250	Each	69.0000	4.0000			
												
Bolt												

7/29/09 3:11

(1)

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST 69

109632 1

110382 18

111650 50

7/29/09 6:50

MS21042L6		Purchased	No			250	Each	755.0000	6.0000			
												
Nut												

7/29/09 3:11 (1)

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST 755

105077 22

110002 233

111548 100

111578 400

7/29/09 2

July 28, 2009 1:55:31 PM

Shop Packet Print

Page 4

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

July 28, 2009 1:55:31 PM

Work Order ID: 50980

Parent Item: D212-664-101RevC

Parent Item Name: Crosstube Fwd

Comments:

Start Date: 7/30/09

Required Date: 8/14/09

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
AN960JD616		Purchased	No			250	Each	326.0000	18.0000 ✓			



Washer

Rec'd 8/3/09 (1)

<u>Warehouse</u>	<u>Loc Qty</u>	<u>Loc Code</u>
<u>Location</u>		
Main Warehouse		
ST	326	
107242	3	
107959	6	
109371	8	
110704	23	
111193	18	
111607	268	

m/1 2314

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____


Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DART AEROSPACE LTD		Work Order:	850980
Description: Crosstube High Fwd (205/212/412)		Part Number:	D212-664-101
Inspection Dwg: D212-664-141 Rev: C		Page 1 of 1	

Required Dimension	Min	Max
Height	26.79	27.05
1/2 Span	53.59	53.85
Angle	49	52
Total Span	107.18	107.7

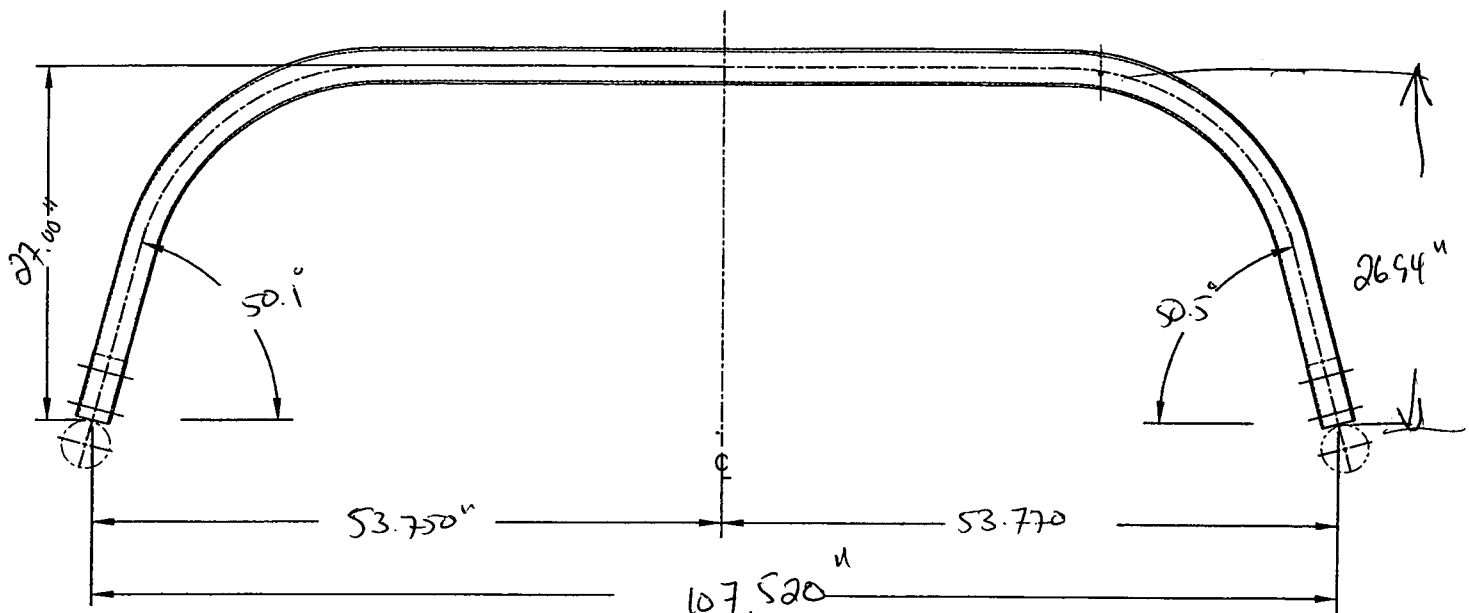

Comments
* tube is a little off from height from side to side

QC15 Inspection	S
Date	07/05/14

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	07.05.31	Dimensions updated per Dwg Rev C	KJ/JM	



RELEASED

07.04.24

DEO ATTACHED

DESIGN PH	DRAWN BY PH	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED QP	APPROVED PH	DRAWING NO. D212-664-141	REV. C SHEET 1 OF 3
DATE 07.03.08		TITLE XTUBE ASS'Y (205/212/412 HI FWD)	SCALE NTS
A	00.12.12	NEW ISSUE	
B	05.02.04	ADD HOLES FOR COMPATABILITY WITH BHT/AA SKIDTUBES	
C	07.03.08	REMOVE -851 ABRASION STRIP; ADD MAGNOBOND 6398, CUSHION, REVERSE CLAMPS	






Qty	Part Number	Description
X	D212-664-141	CROSSTUBE ASSEMBLY (205/212/412 HIGH FWD)
1	D6005-128	CROSSTUBE
2	D2893-1	SUPPORT
4	D3595-063-450	RUBBER CUSHION
4	MS21920-25	CLAMP (OR MS21920-26)
A/R	MAGNOBOND 6398	ROCKWELL SPECIFICATION RBO-120-023 ADHESIVE (TEXTRON/BELL SPEC. 299-947-100, TYPE II, CLASS 2 ADHESIVE)

GENERAL NOTES:

- 1) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- 2) MATERIAL: MANUFACTURED FROM D6005-128
FINISHED LENGTH = 126.51±0.020
- 3) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 4) PART IS SYMMETRIC ABOUT CENTERLINE.
- 5) RUN-OFF PART. BLEND OUT EDGE LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH.
- 6) BEND PROGRESSIVELY WITH A MINIMUM OF 3 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 7) LIQUID PENETRANT INSPECT OUTSIDE SURFACE OF CROSSTUBE PER QSI 038.
- 8) SCRIBE DART PART NUMBER AND BATCH NUMBER IN THIS AREA WITH VIBRATING STYLUS.
- 9) INSTALL D2893-1 SUPPORT USING 0.03" TO 0.06" THICK LAYER OF MAGNOBOND 6398 PER QSI 015. LET CURE FOR 12 HOURS AFTER INSTALLATION AND PRIOR TO PACKAGING.
- 10) INSTALL MS21920-25 CLAMPS (OR -26) WITH D3595-063-450 RUBBER CUSHIONS TO SECURE THE D2893-1 SUPPORT ON TOP SIDE OF THE CROSSTUBE. ENSURE CLAMPS ARE OPPOSITE OF CROSSTUBE SUPPORT
- 11) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE.
- 12) TORQUE CLAMPS 80 TO 100 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING.

Copyright © 2000 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

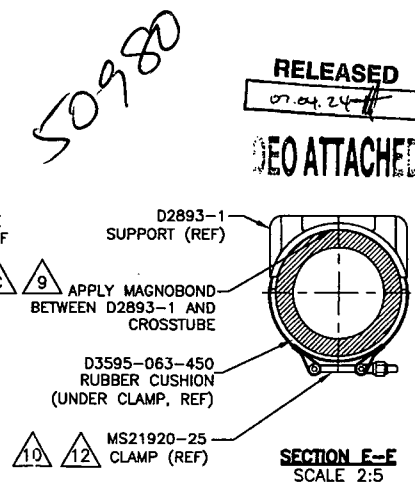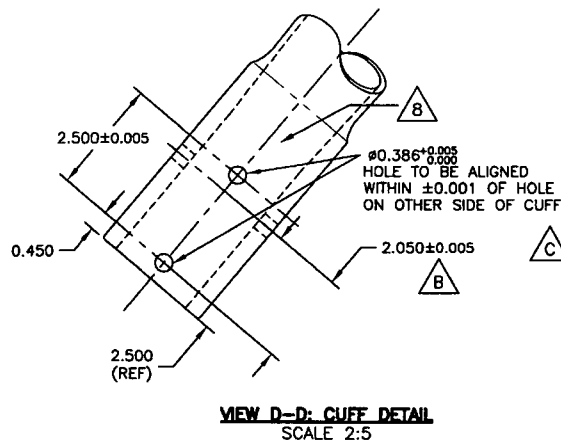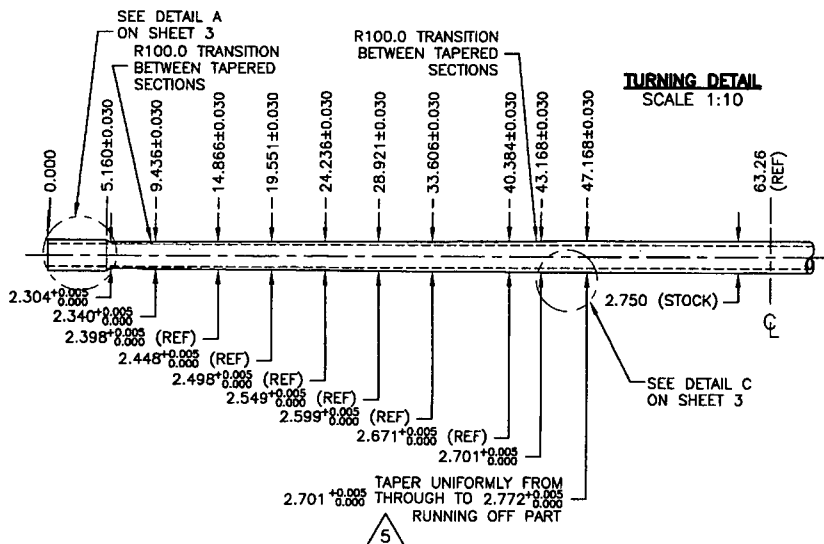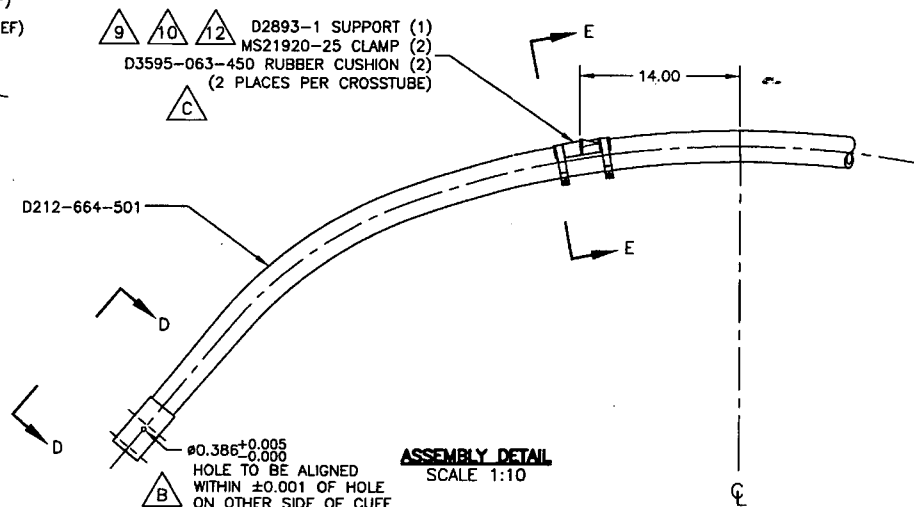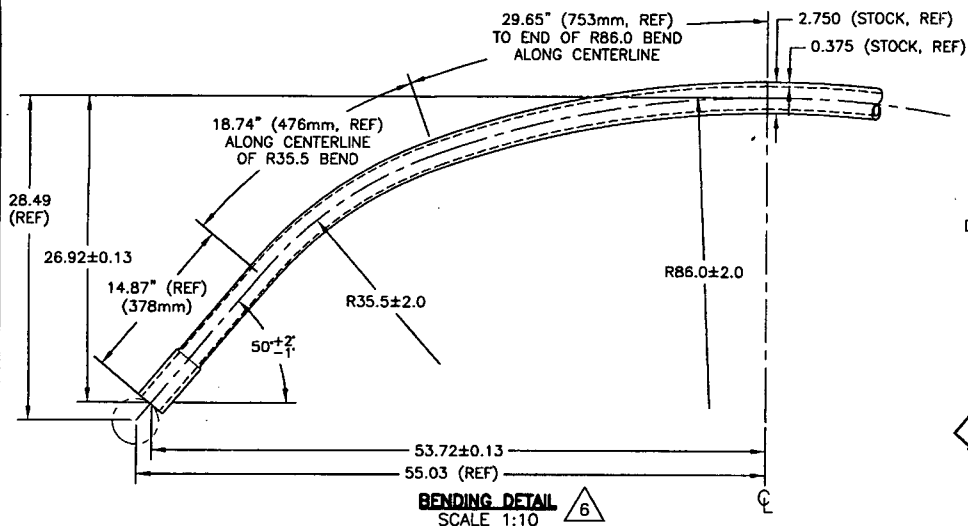

COPYRIGHT © 2000 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.


DESIGN	PH	DRAWN BY	PH	DART	DART AEROSPACE LTD. HARRISBURG, ONTARIO, CANADA
CHECKED	97	APPROVED	4	DRAWING NO.	REV. C
DATE	07.03.08	TITLE	XTUBE ASS'Y (205/212/412 HI FWD)	SCALE	SHEET 2 OF 3

RELEASED
67.04.24 (P)
PER E.C.N. 897


DEO ATTACHED

50980


DETAIL A: CROSSTUBE CUFF

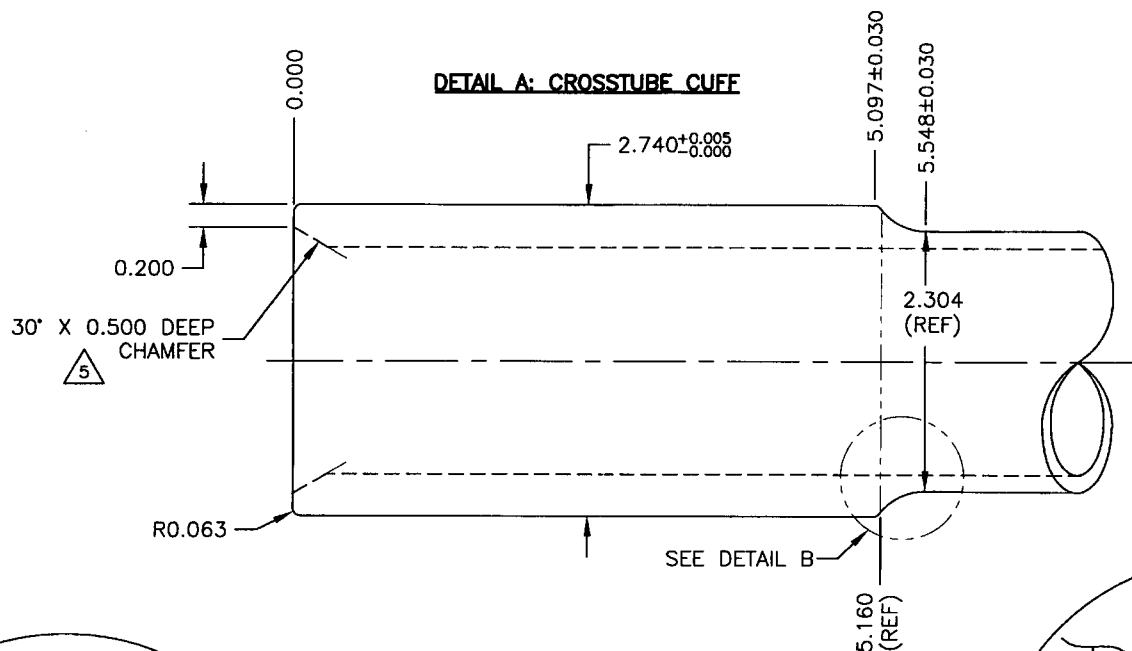

**DETAIL B: CUFF
TRANSITION
SCALE 4:1**

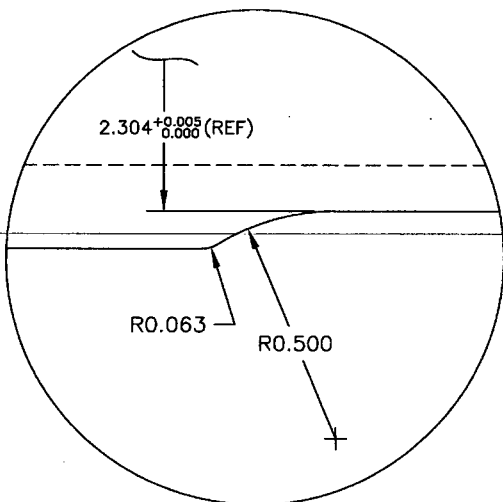

**DETAIL C:
TAPER RUN-OFF
NOT TO SCALE**

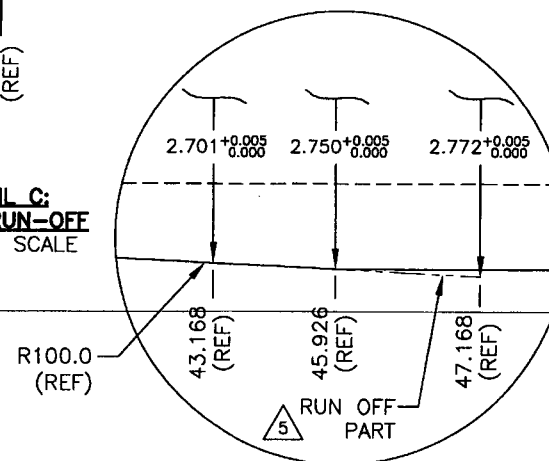

COPYRIGHT © 2000 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL
AND IS SUPPLIED ON THE EXPRESS CONDITION
THAT IT IS NOT TO BE USED FOR ANY PURPOSE
OR COPIED OR COMMUNICATED TO ANY OTHER
PERSON WITHOUT WRITTEN PERMISSION FROM
DART AEROSPACE LTD.

DESIGN PH	DRAWN BY PH	DART	DART AEROSPACE LTD. MARKHAM, ONTARIO, CANADA
CHECKED J	APPROVED J	DRAWING NO. D212-664-141	REV. C SHEET 3 OF 3
DATE 07.03.08	TITLE XTUBE ASS'Y (205/212/412 HI FWD)	SCALE 1:1	

DRAWING NO. D212-664-141	TITLE CROSSTUBE	REV. C	DART AEROSPACE LTD ENGINEERING ORDER		D.E.O. NO. D212-664-141-C-1	SHEET NO. SHEET 1 OF 1	SCALE NTS
DRAWN <i>AD</i>	CHECKED <i>RS</i>	MFG. APPR. <i>EA</i>	APPROVED <i>AD</i>		DE APPR. <i>AD</i>		
DATE 09.05.01	DATE 09.06.15	DATE 09.06.15	DATE 09/06/16		DATE 09/06/16		

CHANGE:

ADD THE FOLLOWING CROSSTUBE ASSEMBLY:

Part Number	Description
D212-664-141B	CROSSTUBE ASSEMBLY (214 HIGH FWD)

THE D212-664-141B CROSSTUBE HAS THE SAME PARTS LIST AS THE D212-664-141 CROSSTUBE. HOWEVER, INSTALL THE SUPPORTS AS SHOWN IN FIGURE 1 OF THIS ENGINEERING ORDER. THE NEW KIT IS OTHERWISE ASSEMBLED PER THE D212-664-141 CROSSTUBE.

RELEASED
09/06/16

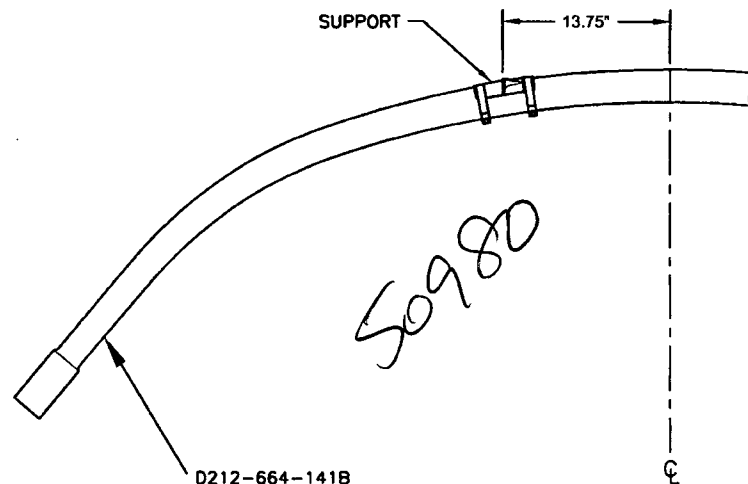


FIGURE 1 - SUPPORT INSTALLATION

5.0 PARTS LIST

5.1 HIGH GEAR CROSSTUBES

Item	-101	-201	-203	Part Number	Description
	X			D212-664-101	CROSSTUBE INSTALLATION, 204/205/210/212/214/412, UH-1H, UH-1A/B/E/F/L/P, TH-1F/L, HH-1K HIGH FWD
		X		D212-664-201	CROSSTUBE INSTALLATION, 204/205/210/212/214, UH-1H, UH-1A/B/E/F/L/P, TH-1F/L, HH-1K HIGH AFT
			X	D412-664-203	CROSSTUBE INSTALLATION, 412 HIGH AFT
1	1			D212-664-141	CROSSTUBE ASSEMBLY, 204/205/210/212/214/412, UH-1H, UH-1A/B/E/F/L/P, TH-1F/L, HH-1K HIGH FWD
2		1		D212-664-241	CROSSTUBE ASSEMBLY, 204/205/210/212/214, UH-1H, UH-1A/B/E/F/L/P, TH-1F/L, HH-1K HIGH AFT
3			1	D412-664-243	CROSSTUBE ASSEMBLY, 412 HIGH AFT
10	2			* D2893-1	SUPPORT
11	4			* D3595-063-450	RUBBER CUSHION
12	4			* MS21920-25	CLAMP (OR MS21042-26)
13	4			AN6-35A	BOLT
14	4			AN6-36A	BOLT
15	6			MS21042L6	NUT (OR MS21042-6)
16	18			AN960JD616	WASHER
20		2		* D2940-1	SUPPORT
21		4		* D3595-063-530	RUBBER CUSHION
22		4		* MS21920-28	CLAMP (OR MS21042-30)
23		4		AN6-40A	BOLT
24		2		AN6-41A	BOLT
25		6		MS21042L6	NUT (OR MS21042-6)
26		18		AN960JD616	WASHER
30			1	* D2896-1	SUPPORT
31			2	* D2856-600-1009	ABRASION STRIP
32			2	* D3595-063-570	RUBBER CUSHION
33			4	* MS21920-28	CLAMP
34			2	* MS21920-30	CLAMP (OR MS21042-32)
35			4	AN6-40A	BOLT
36			2	AN6-41A	BOLT
37			6	MS21042L6	NUT (OR MS21042-6)
38			18	AN960JD616	WASHER
39			2	* D3189-1	CHAFING SHIELD
50	1	1		D3428-1	PLACARD

*REFERENCE ONLY. PARTS ARE INCLUDED IN D212-664-141/-241 OR D412-664-243 ASSEMBLIES ABOVE
NOTE: KITS INCLUDE EXTRA HARDWARE FOR COMPATIBILITY WITH BOTH DART AND BELL/AA
SKIDTUBES.

• COPYRIGHT © 2001 BY DART AEROSPACE LTD. •
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED
OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

Revision: F

Date: 08.09.05

50980



P- 14947

SIGNATURES			
CLIENT REPRESENTATIVE	<u>Matt Muroch</u> PRINT	<u>Matthew Muroch</u> SIGNATURE	DTR # <u>E-20071</u>
TECHNICIAN (SIGNATURE):	<u>[Signature]</u>		REPORT REVIEWED BY:
NAME (PRINT):	<u>Mike Johnston</u> 1 ST TECHNICIAN	<u></u> 2 ND TECHNICIAN	NAME INITIALS
CGSB LEVEL <u>II</u> SNT LEVEL <u></u>	CGSB LEVEL <u></u> SNT LEVEL <u></u>		
CGSB REG. NO <u>6066</u>	CGSB REG. NO <u></u>		
